



Work Part plan – May 13
Replace Signs in Airpark
Perform Maintenance on Gates

Results: replaced 2 stop signs, 2 sign posts, ~10 no parking signs
Trimmed around a number of signs
Performed maintenance on south gate





2 new stop signs installed
New post
Trimmed weeds and grass



Replaced 2 posts and ~10 signs



Gate maintenance (south gate)
Tighten and lube chain (was dragging)
Straighten top rail
Adjust bottom rail spacing
Adjust drive belt








Work remaining
Trim around signs



Work remaining
Additional signs
Street end barrier boards replaced



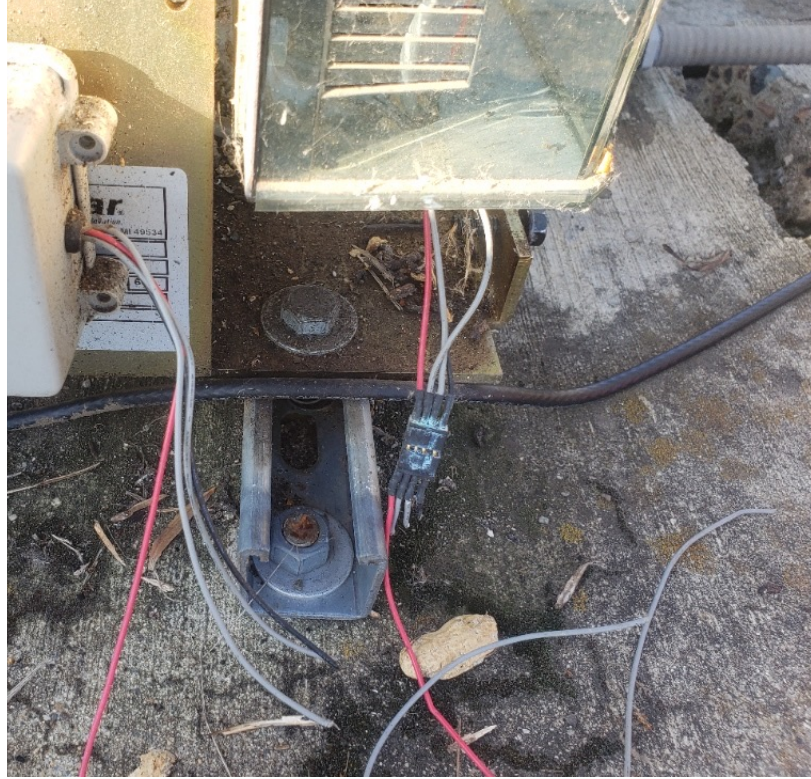

North gate wiring previously repaired
Needs rails aligned and cable run

Next workday June 3rd

Priority tasks:

- Airpark:
 - North gate maintenance
 - Trim around signs, replace 2 stop signs
- Airport:
 - Weed trimming around lights needs to be repeated
 - Tie down parking needs weeds trimmed
 - Mowing needs to be scheduled
 - need weed trimmers and light spotters available
- Battery box locks on anti-collision lights

project	lead	tasks	tools/supplies	training	follow-up
gates		clean and lubricate	chain lub, grease gun	operation and maintenance manual	
		check stops			
		check and adjust rails	laser tracker, wrenches		
		check and adjust chain slack	tape measure, wrenches	allowable slack	
tie downs					
		check condition			
		weed around	weed trimmer		
		remove chains, locks	bolt cutters, cutoff grinder		
		spray weedkiller			
